

**Zeitschrift:** IABSE congress report = Rapport du congrès AIPC = IVBH  
Kongressbericht

**Band:** 14 (1992)

**Artikel:** Railway bridges constructed by precast segmental construction method

**Autor:** Raghavan, N. / Sarangdhar, M.C. / Kanitkar, V.K.

**DOI:** <https://doi.org/10.5169/seals-13856>

### **Nutzungsbedingungen**

Die ETH-Bibliothek ist die Anbieterin der digitalisierten Zeitschriften auf E-Periodica. Sie besitzt keine Urheberrechte an den Zeitschriften und ist nicht verantwortlich für deren Inhalte. Die Rechte liegen in der Regel bei den Herausgebern beziehungsweise den externen Rechteinhabern. Das Veröffentlichen von Bildern in Print- und Online-Publikationen sowie auf Social Media-Kanälen oder Webseiten ist nur mit vorheriger Genehmigung der Rechteinhaber erlaubt. [Mehr erfahren](#)

### **Conditions d'utilisation**

L'ETH Library est le fournisseur des revues numérisées. Elle ne détient aucun droit d'auteur sur les revues et n'est pas responsable de leur contenu. En règle générale, les droits sont détenus par les éditeurs ou les détenteurs de droits externes. La reproduction d'images dans des publications imprimées ou en ligne ainsi que sur des canaux de médias sociaux ou des sites web n'est autorisée qu'avec l'accord préalable des détenteurs des droits. [En savoir plus](#)

### **Terms of use**

The ETH Library is the provider of the digitised journals. It does not own any copyrights to the journals and is not responsible for their content. The rights usually lie with the publishers or the external rights holders. Publishing images in print and online publications, as well as on social media channels or websites, is only permitted with the prior consent of the rights holders. [Find out more](#)

**Download PDF:** 10.08.2025

**ETH-Bibliothek Zürich, E-Periodica, <https://www.e-periodica.ch>**



## **Railway Bridges Constructed by Precast Segmental Construction Method**

Ponts-rails construits à l'aide de voussoirs préfabriqués

Eisenbahnbrücken aus vorgefertigten Elementen

### **N. RAGHAVAN**

Princ. Consult.  
STUP Consultants Ltd.  
Bombay, India

### **M.C. SARANGDHAR**

Princ. Consult.  
STUP Consultants Ltd.  
Bombay, India

### **V.K. KANITKAR**

Princ. Consult.  
STUP Consultants Ltd.  
Bombay, India

## **1. GENERAL FEATURES**

Railway bridges in India have so far been predominantly constructed using structural steel and only over the last decade or so prestressed concrete has come to be used as a construction material for superstructure of railway bridges. For three railway bridges located over marine backwaters near Cochin spread over about 5 Km length, prestressed concrete box girders constructed by precast segmental construction were adopted. The three bridges had 29, 5 and 4 simply supported spans respectively of 30.5 m length. Lack of adequate space and other site constraints restricted any major casting work at or near the site. Hence conventional cast in-situ working or precasting at site or elsewhere and launching the girders were ruled out. A system of precast segmental construction was adopted for these railway bridges for the first time in India.

## **2. PRECASTING**

The girders were precast in seven segments by the match-cast long line system at a centralised precasting yard located about five kilometers from the site. Shear keys were provided on the matching faces. A travelling portal gantry was provided in the yard to handle the segments from casting bed to stacking beds and then on to a launching jetty supported on pipe piles. From there the segments were taken to the different sites on a pontoon towed by a tug. The maximum weight of a segment was about 35 t. Concrete brackets were provided to facilitate lifting of the girder in future to replace the neoprene bearings. Provisions for adding cables in future, if required, have been made.

## **3. ASSEMBLING**

A travelling assembly truss system consisting of two independent rectangular trusses of about one and one-third span length was adopted for assembling the segments. Underslung cross trusses spanning between the main trusses supported the segments. An overhead crab travelling over the top of the main trusses picked up the segments from the pontoon below and placed them on the cross trusses. All segments were thus placed on the assembly truss with gaps in between. After applying an epoxy formulation on the match-cast faces, the segments were pressed together using temporary prestressing to cure the epoxy under pressure. Temporary prestressing was applied using HTS strands on top of deck slab and on soffit slab of the box girder. Thereafter permanent cables were threaded through, stressed and grouted. After assembling one span the

trusses were shifted to the next span, with the front end resting over a trestle mounted pontoon and the rear end resting on a trolley moving over the previously erected span. After completing one bridge the assembly trusses were partially dismantled and taken to the next bridge. Thereafter finishing operations were carried out on the girders.

#### 4. CONCLUSION

The precast segmental construction system proved to be the optimum solution for this site. A maximum speed of one span per week could be achieved with this methodology. The owners of the project are Southern Railways and the contractors, M/s. Bhagheeratha Engineering Ltd. M/s. STUP Consultants Limited provided design and construction consultancy services to the contractor.

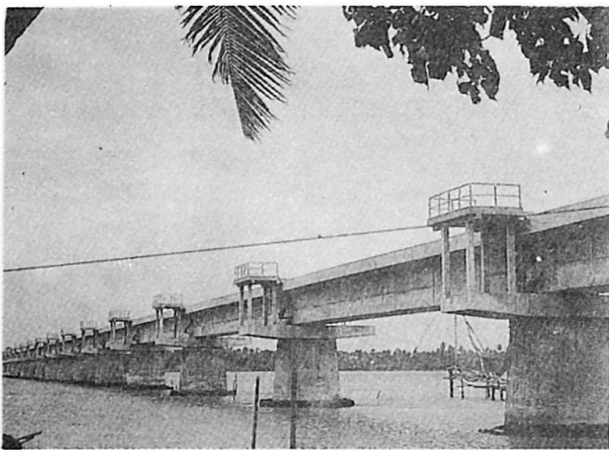


Fig. 1 Bridge at Aroor-Kumbalam

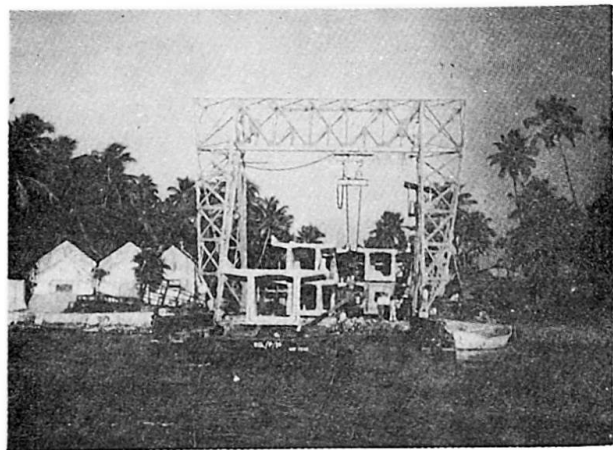


Fig. 2 Casting Yard

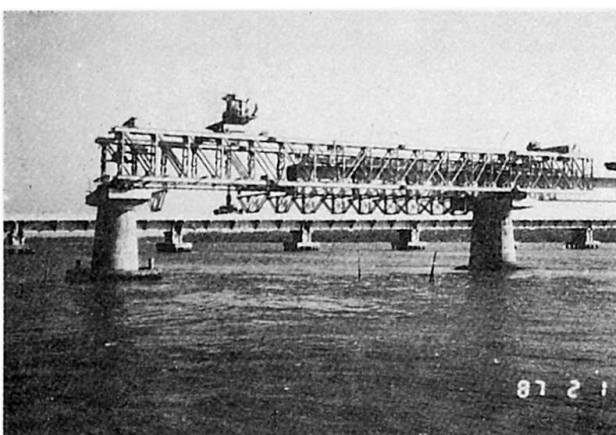


Fig. 3 Assembly of Segment



Fig. 4 Movement of Assembly Truss
