Zeitschrift: IABSE congress report = Rapport du congrès AIPC = IVBH

Kongressbericht

Band: 12 (1984)

Artikel: Engineering construction management projects at Singapore Airport

Autor: Lim, Boon Liang

DOI: https://doi.org/10.5169/seals-12112

Nutzungsbedingungen

Die ETH-Bibliothek ist die Anbieterin der digitalisierten Zeitschriften auf E-Periodica. Sie besitzt keine Urheberrechte an den Zeitschriften und ist nicht verantwortlich für deren Inhalte. Die Rechte liegen in der Regel bei den Herausgebern beziehungsweise den externen Rechteinhabern. Das Veröffentlichen von Bildern in Print- und Online-Publikationen sowie auf Social Media-Kanälen oder Webseiten ist nur mit vorheriger Genehmigung der Rechteinhaber erlaubt. Mehr erfahren

Conditions d'utilisation

L'ETH Library est le fournisseur des revues numérisées. Elle ne détient aucun droit d'auteur sur les revues et n'est pas responsable de leur contenu. En règle générale, les droits sont détenus par les éditeurs ou les détenteurs de droits externes. La reproduction d'images dans des publications imprimées ou en ligne ainsi que sur des canaux de médias sociaux ou des sites web n'est autorisée qu'avec l'accord préalable des détenteurs des droits. En savoir plus

Terms of use

The ETH Library is the provider of the digitised journals. It does not own any copyrights to the journals and is not responsible for their content. The rights usually lie with the publishers or the external rights holders. Publishing images in print and online publications, as well as on social media channels or websites, is only permitted with the prior consent of the rights holders. Find out more

Download PDF: 10.07.2025

ETH-Bibliothek Zürich, E-Periodica, https://www.e-periodica.ch



Engineering Construction Management Projects at Singapore Airport

Gestion de la construction de l'aéroport de Singapour

Projekt und Management-Organisation des Flughafens in Singapore

Boon Liang LIM
Property Dev. Mgr.
Singapore Int. Airlines
Singapore



Boon Liang Lim, a 42 year old Singaporean, was educated locally. He worked with Bank Group: Management Services Subsidiary as a Project Executive, then a Project Supt. for the airline before becoming its Property Development Manager for almost 11 years.

SUMMARY

The new Changi Airport near Singapore was designed and built in four years, from 1977 till 1981. A technical description of the project and the construction management organization of the Changi Development Unit are presented.

RESUME

Le nouvel aéroport de Changi près de Singapour a été étudié et construit en quatre ans, de 1977 à 1981. La description technique et l'organisation de la gestion du projet de la "Changi Development Unit" sont présentés.

ZUSAMMENFASSUNG

Der neue Changi Flughafen bei Singapore wurde in vier Jahren, von 1977 bis 1981, projektiert und ausgeführt. Die technische Beschreibung des Projektes und die Management-Organisation der "Changi Development Unit" werden vorgestellt.



PROJECT HISTORY

The Changi before was the idyllic tropical seaside resort - rusticated in many ways shown by the kampong settlements, vegetable farms, fruit orchards and picnicker camps. The Changi now/after is the airport of the twenty-first century - a bustling terminal of 4,400 pax turnover per peak hour, 30,000 meals per day, 750 tons of freight per day and 80 aircraft movement per hour (capacity). What's How's and Why's went on behind the hectic 6-year transformation programme from May 1975 till July 1981 with the \$1.500(B) total investment, including SIA Group of \$0.500(B).

Buoyant air traffic forecast shown by Fig. 1 on annual air passengers, air cargo handled and aircraft movements make it extremely difficult to continue at Paya Lebar: firstly, resettlement squatter families of easily 50 times of Changi; secondly, a second runway would entail straddling over a river and the decade old MOE refuse dump; thirdly, the South flight path hovers above high density, high rise public housing and fourthly, relying on ad hoc and improvised expansion expedients is unsatisfactory. Changi offers tremendous prospects - it is a totally greenfield site. 900 hectares of land were reclaimed from the sea. The total airport area (Fig. 2) is about 2500 m x 6500 m or 1663 hectares. Each of the two parallel runways has a max. capacity of 40 movements per hour. A total of 46 passenger aircraft, 6 cargo aircraft and 3 maintenance parking positions are provided. A terminal building of 120 m x 204 m, five stores high, two finger docks each 580 m long, a hangar building and several other buildings were already realized in phase I. Air safety and noise protection are safeguarded and, above all, unencumbered expansion potential.

The project development and milestones are shown in Fig. 2. The abbreviations are explained in the index at the end of the paper.


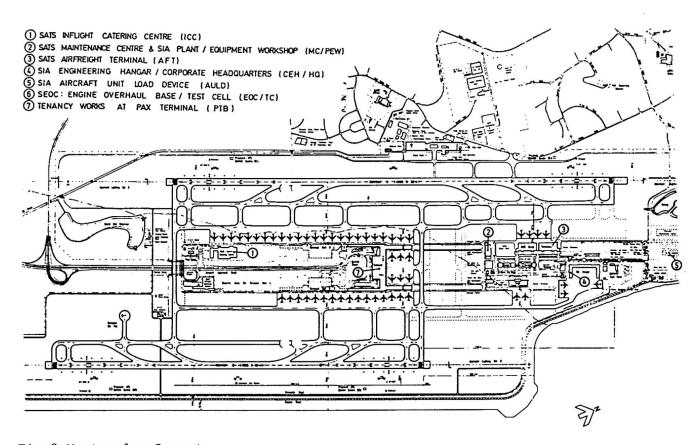


Fig.2 Masterplan Layout



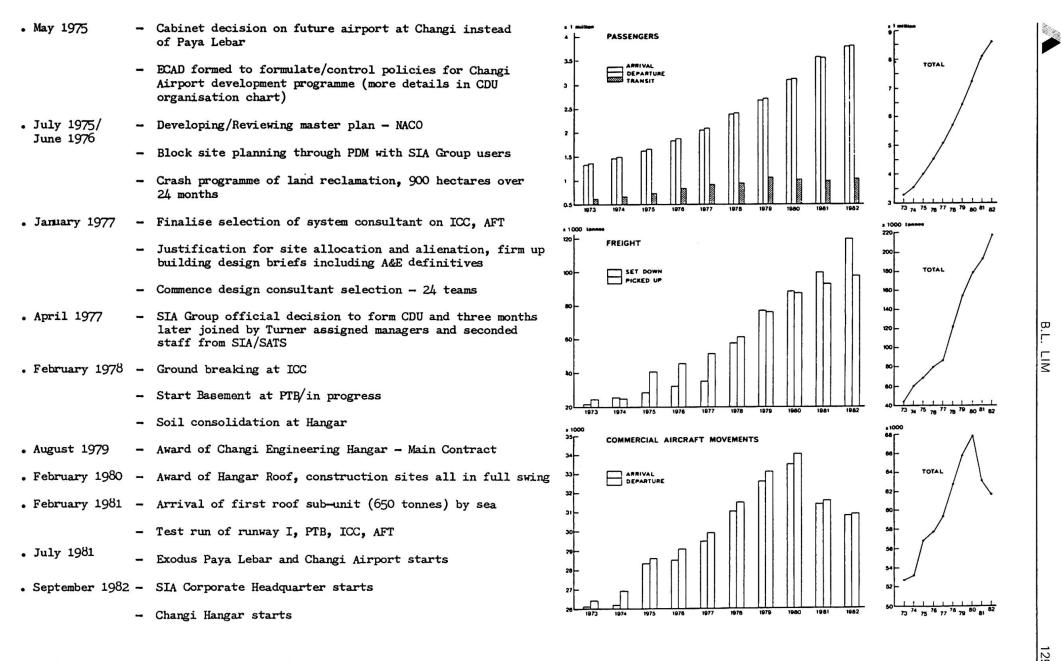

TECHNICAL DESCRIPTION

A few features taken from the key projects (Fig. 3)

		<u>m2</u>	Cost (SIN \$)
	SATS Airfreight Terminal (AFT)	42,000	72.000 (M)
	SATS Inflight Catering Centre (ICC)	50,000	80.000 (M)
•	SIA Corporate Headquarters (CEH.2)	30,000	225 000 (M)
	SIA Engineering Hangar (CEH.1)	21,000	225.000 (M)

Airfreight Terminal. Done on strictly "function first and form later" by commissioning BNP to do all economic studies/review, system engineering and only after completion of system flow and layout and the Building Design Brief, the Building Consultant got on board to wrap around the process flow layout. The first phase comprises symmetrically placed site, modules 2 and 3 capable of expanding to M1 and M4 to double up the initial capacity of 300,000 thru-put freight tonnes to 600,000 FT. The internal features show the modern methods of material handling system by elevated transfer vehicle (ETV) and high level storage racks through use of retrieval cranes.

Inflight Catering Centre. Similarly done as for AFT. System experts on mass meal production were appointed to carry out a thorough review of traffic analysis (by computer model simulation). A system of layout flow processers, storage support sub systems, wash-up subsystem was developed on a participatory approach with all related users. A building design brief containing the "A&E Definitives" was jointly developed with CDU before the Building Design Consultants were selected. The design development was exhaustive capitalising on the confluence of expertise from 4 sources: the System Experts, Inhouse Catering, Management Knowhow, CDU Project Management and the long standing and eminent Architects, Engineers and Quantity Surveyors. Planned on modular grids the present capability of 30,000 meals per day can be easily expanded to 50,000 per day in the 1990's.

SIA Corporate Headquarters. Located at the upper 5 floors of the U-shape on plan, 10-storey annexe, SIA Head Office shows a modern office system approach. In conjunction with the Accoustic Consultants, the Architects and Engineers, CDU's inhouse landscape open plan unit (LMU) in consultation with a German team (QBT) implemented the first open plan office of the 30,000 m2 scale at the annexe. The physical results are achieved through fine tuned co-ordination efforts - LMU, Design Consultants, Contractors, the end users and the specialist open plan furniture vendors.

Changi Engineering Hangar (CEH). Again, the successful completion is accomplished through collaborative efforts of design consultants, specialist contractors and in the case of the tubular diagrid roof the unstinted contribution of the Checking Consultant Engineer. The Tubular Space Frame Diagrid Roof solution was the combined result of poor site condition and height constraint. However, the design, services co-ordination, fabrication and final site erection and lifting of the 2,500 tonnes of the 218(L) x 92(D) x 8(H) columnfree roof structure is a construction planning and management operation worth of attention to future practitioners or clients facing the same problem. Even the last expected activity could go wrong, if no advanced preparing as well as corrective action planning to face up situation had been provided. The case of protective coating is a classic example.





Soil Consolidation. Because of an underlying lens-shape section structure of thick marine clay, the site had to be subject to 14 months surcharge varying 6-8 meters high plus stitched down castle board drain at approximately 2.00 m centres at a total costs of \$5.00(M).

Flying Table Forms. Owing to slow start-up due to site conditions and another reason, the Construction Team collaborated with the Contractor to use this system of formwork. Productivity rose from 31 days per floor to an all-time high of 18 days per floor at the 9th and 10th floor slab. Records confirm a time saving of 25% over the conventional formwork method.

EXECUTIVE PROJECT MANAGEMENT ORGANISATION

Ideals shown in our objective on design/approaches are one thing but follow-up action is another. There was the large scale of some 304,000 m2 of total gross built-up area scattered over six far flung sites. Another couple of worrysome features were the near \$500.00(M) budget and the very tight time frame of 4 years for design and construction, discounting 11/2 years for masterplanning of the total project duration.

While mobilising inhouse development expertise and user departments for masterplanning and building design briefs went underway it was at the 2nd quarter of 1977 when the Changi Development Unit (CDU) was set up and put into operation.

It was intended to be the pure type of project or indeed a construction management organisation to be run independently with minimum interference and maximum support from SIA/SATS top management. The organisation is accountable to both SIA/ SATS management separately - implemented by monthly series of high level project management meetings (Fig. 3).

The Property Development Manager (Changi Projects) is represented in the Executive Committee on Airport Development (ECAD) to provide the organisation links (Fig.4). He also submitted monthly status as well as financial management report to the Group Chairman.

CDU's mission was to ensure effective project funds control, time schedule and quality of the works. All the three (3) wings, namely, Project Engineering, Construction Control and General & Administration are mutually supportive to carry out its mission during 4-5 years. Its own facilities included a 1.000 m2 two-storey CDU rented building, photostat and blue print equipment, word processor, 2 landover vehicles and some other sundry equipments/site facilities.

Some matrix relationship lines were inevitable as eventually the project engineers, construction superintendents had to work closely with end users, airport building authorities, innumerable consultant staff, contractors supervisory and management personnel.

In view of the different form of employment contracts, man-management grew sometimes to awkward proportions. The composition of the CDU at peak is:

(a) second SIA/SATS


(b) contract personnel

52

(c) assigned TEA

6 102

TEA personnel enjoyed relatively generous compensation being assigned through the project management contract, contract staff receive very high salary but reduced

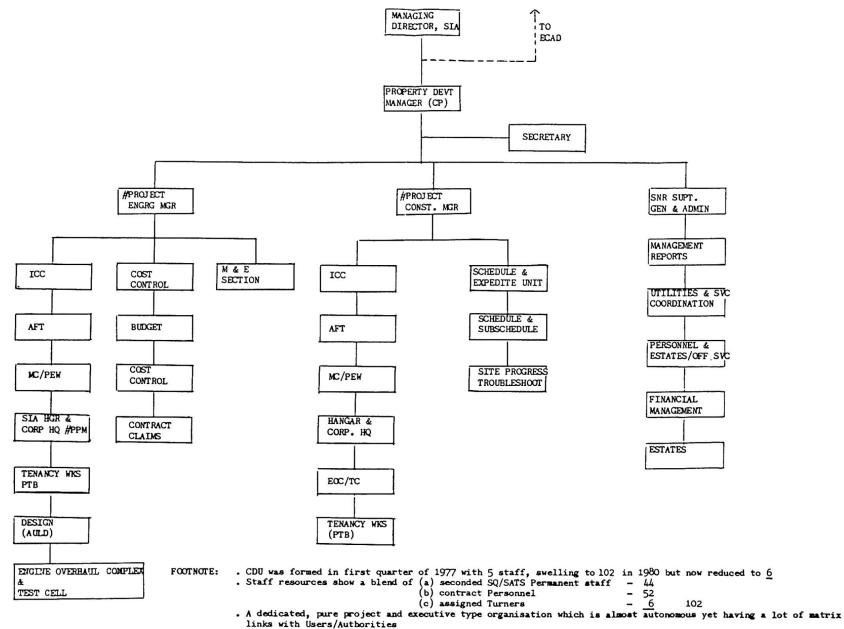



fringe benefits compared with the seconded permanent staff. All the conflicts were resolved after a series of meetings and compromises as the threat of quitting their jobs to disrupt the project was more real than imagined.

Imbued with humanist school of thinking, CDU Admin actively promoted several programmes to forge close knit team spirit i.e.

- (a) Inter site sports competition and cross country run
- (b) CDU Annual Dinner & Dance and X'mas Do's
- (c) Visits to Homes of Handicaps, Aged, Salvation Army, etc

Quality Control Circles (QCC) and Open Appraisal Interviews were extensively used.

It is to be noted that all contracts were carried out on a "design and build" basis except the 747 Test Cell which was one on turnkey. Budget and schedule control were practised by means of cost commitment and payment reports, variance procedures, milestone/stage programme tracking and updating.

CONCLUSIONS

Experience is the greatest teacher of all lessons. Having lived through all the difficult phases of the projects, we realise that short lead times have to be treated seriously. Advanced preparation is the safeguard. Diligence and dedication cannot find substitutes in whatever project tools or systems.

In general appraisal, we have fared fairly well. The benefits of a well structured project management system are vivid. It represents results achieved through cooperative endeavours which are certainly greater than the total sum of the component parts. For the skeptics and followers alike, Changi Airport provides a living model of the synergistic efforts of international expertise, technological advancements and the local resources of people and marginal land availability.



ETV

:

LIST OF ABBREVIATIONS/ACRONYMS

ECAD Executive Committee on Airport Development (headed by the Chief Permanent Secretary Singapore Government after being formed by Cabinet Decision in May 1975). DCA Department of Civil Aviation which is part of the : Ministry of Communication. CADD Changi Airport Development Division i.e. specially formed by Public Works Department to do all Master Planning, Infrastructure, Pax Terminal and other services buildings. Changi Development Unit formed by SIA Group Management CDU : to handle the Group's major projects worth over (B)0.500 Singapore Dollars. MOE : Ministry of Environment NACO : Netherland Airport Consultancy A & E : Architectural and Engineering M & E Mechanical and Electrical ATC Air Traffic Control (Tower) : SATS : Singapore Airport Terminal Services SADE : Singapore Airport Duty-Free Emporium SEOC : Singapore Engine Overhaul Centre TEA Turner East Asia : CEH : SIA Changi Engineering Hangar ICC: Inflight Catering Centre AFT : Airfreight Terminal MC : Maintenance Centre for apron handling equipment PEW : Plant & Equipment for engineering ground equipment AULD : Aircraft Unit Load Device i.e. aircraft container PTB : Passenger Terminal Building

Elevated Transfer Vehicle



REFERENCE MATERIALS

12. Straits Times Commemorative

- 1979

Feature on SIA Group Projects

SECTION

Background Materials

1.	Airport Forum 4/81	Background Data
2.	Proceedings of Airport Planning and Development Symposium - 1982	Background Data
3•	Department of Civil Aviation: Annual Report 1977 till 1982	Growth Statistics Background
4•	Implementation of Project Management by Project Management Institute, California USA	Executive and Autonomous Project Management Organisation and Organisation Styles
5•	Selected Readings of Human Resources Managment and Productivity by Bill Reddin	Humanist Approach and QCC's
6.	Managing Human Resources by Sayles and Straus	Humanist Style and Open Appraisal
7•	Project Manual on Financial Controls and PMIS by Arthur Anderson	Financial Controls
8.	Programming Method - HM SO	Scheduling Controls
9.	Management Techniques - by Oxley and Posket	Scheduling Controls
10.	Principles of Construction Management by Roy Pilcher	Programming and General Interest
11.	Management of Engineering Projects by Maurice Snowdon	General Interest
